




# CENTRAL AREA SEWER SEPARATION PROGRAM POTENTIAL CONSTRUCTION PHASING

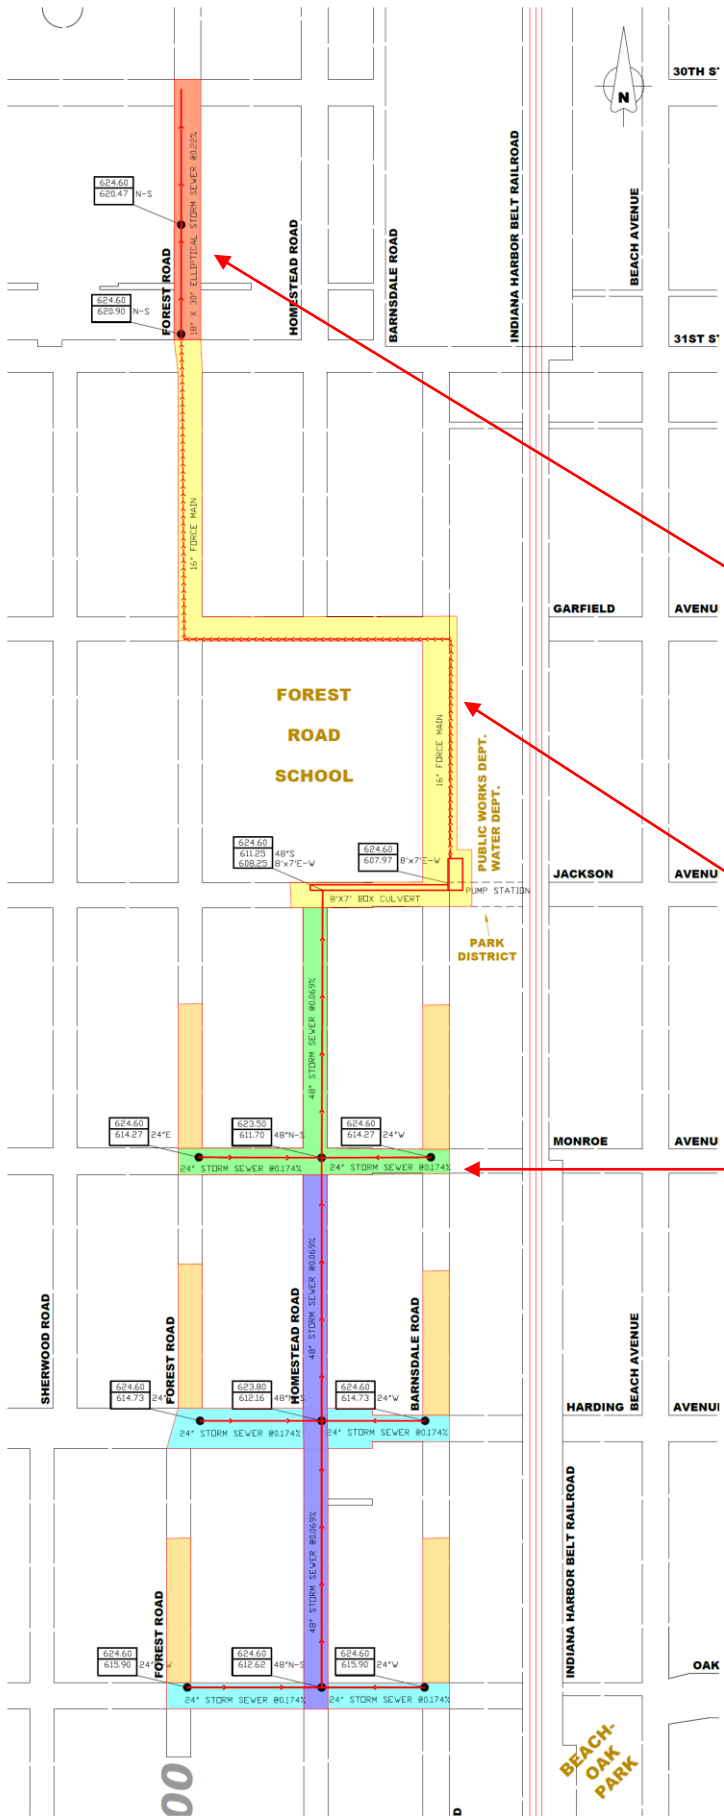

## PHASE I

CONSTRUCT A 18"x30" ELLIPTICAL STORM SEWER ON FOREST ROAD FROM 30TH STREET TO 31ST STREET.

\$440,000.00

## PHASE II

CONSTRUCT A 8'x 7' BOX CULVERT ON JACKSON AVENUE FROM BARNSDALE ROAD TO HOMESTEAD ROAD, THE INSTALLATION OF A 8,000 GPM PUMP STATION AT PUBLIC WORKS SITE (NORTHEAST CORNER OF JACKSON AVENUE AND BARNSDALE ROAD), AND THE INSTALLATION OF A 16" FORCE MAIN ON BARNSDALE ROAD, GARFIELD AVENUE AND FOREST ROAD TO 31ST STREET.

\$2,620,000.00

## PHASE III

CONSTRUCT A 48" STORM SEWER ON HOMESTEAD ROAD FROM JACKSON AVENUE TO MONROE AVENUE AND A 24" STORM SEWER ON MONROE AVENUE FROM BARNSDALE TO FOREST ROAD.

\$1,250,000.00

## PHASE IV

CONSTRUCT A 48" STORM SEWER ON HOMESTEAD ROAD FROM MONROE AVENUE TO OAK AVENUE.

\$1,520,000.00

## PHASES V & VI

CONSTRUCT A 24" STORM SEWER ON HARDING AVENUE AND OAK AVENUE FROM BARNSDALE ROAD TO FOREST ROAD.

\$670,000.00 (PER PHASE)

## PHASE VII

SEWER EXTENSIONS ON BARNSDALE ROAD AND FOREST ROAD TO PICK UP MID-BLOCK DRAINAGE STRUCTURES.

\$1,020,000.00
